

Work Order ID 154784

Wednesday, December 21, 2016 11:55:04 A

154784

Page 1

Item ID: D2432 Accept ***N900040100*** Setup Start ***NS1***
 Revision ID: Stop ***NS2***
 Item Name: Bearpaw 19" X 24"
 Start Date: 12/21/2016 Start Qty: 8.00 ***8*** Cust Item ID:
 Required Date: 1/9/2017 Req'd Qty: 8.00 ***8*** Customer:
 Reference:

Approvals: Process Plan: **DAS 21 9-89** Date: **DEC 21 2016** Tooling: Date: Run Start ***NR1***
 QC: Date: SPC (Y/N): Date: Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
Draw Nbr	Revision Nbr								
D2432	H								
120	FLOW WATER JET	0.00							
120									
Waterjet	Memo	0.20							
FLOW CNC Waterjet	Cut Blank as per D2432 File								
130	HAAS CNC VERTICAL MACHINING #1	0.09							
130									
HAAS 1	Memo	0.60							
HAAS CNC vertical machine #1	1-Inspect material for defects or damage prior to machining 2-Machine as per Folio and Dwg D2432 Identify as D2432F 3-Deburr								
140	QC2- Inspect parts off machine FAI/FAIB	0.00							
140									
QC	Memo	0.01							
Quality Control									

⑧ ∅ 12/12/22

8 ∅ DAS 49 9-89 12/01/06

8 ∅ DAS 44 9-89 17-01-09

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐																																																													
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval																																																									
Description Work Order Deviation				Disposition				Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval																																																									
Root Cause		FAULT CATEGORY																																																															
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐	Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐	Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐	Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐	Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐	Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐	Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐	Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐	LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐	Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐	Past Expiry Date ☐	Manufacturing Process ☐	OTHER :			
Misidentified ☐	Past Due ☐																																																																

Work Order ID 154784***154784***

Page 2

Wednesday, December 21, 2016 11:55:04 A

Item ID: D2432 Accept ***N900040100*** Setup Start ***NS1***
Revision ID: Stop ***NS2***
Item Name: Bearpaw 19" X 24"
Start Date: 12/21/2016 Start Qty: 8.00 ***8*** Cust Item ID:
Required Date: 1/9/2017 Req'd Qty: 8.00 ***8*** Customer:
Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start ***NR1***
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
150	QC8- Inspect parts - second check	0.00							
150									
QC	Memo	0.03				8	0		DAS 08 9-89
Quality Control									
160	Identify as per dwg & Stock Location: <u>ST430A</u>	0.00							
160									
Packaging	Memo	0.01				8	6		DAS 6 9-89
Packaging									JAN 11 2017
170	QC21- Final Inspection - Work Order Release	0.00							
170									
QC	Memo	0.13							DAS 21 9-89
Quality Control									JAN 16 2017

mf
17-1-12

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date :	Step #:	QTY Effective :		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition			
				Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
OTHER : ☐					

Picklist Print

Wednesday, December 21, 2016 11:55:04 AM

Page 1
1

Work Order ID: 154784

154784

Parent Item: D2432

D2432

Parent Item Name: Bearpaw 19" X 24"

Start Date: 12/21/2016

Required Date: 1/9/2017

Start Qty: 8.00

Required Qty: 8.00

Comments: IPP REV:A 12.10.17 AS PER DWG REV.H DD VERF:JLM

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
MUHMWB10		Purchased	No			120	sf	1,058.400	3.7	29.6			

MUHMWB10

UHMW 1" Black - 48"x120" Tivar Mfg.#52480104

on 12/12/22

Location

Loc Qty

Loc Code

MAT018

1058.4

m135013

14

m135913

244.4

m136290

400

m136453

400

31

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date :	Step #:	QTY Effective :		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY			
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐
OTHER :					


DART AEROSPACE LTD		Work Order: 154784
Description: Bearpaw		Part Number: D2432
Inspection Dwg: D2432 Rev: H		Page 1 of 1

FIRST ARTICLE INSPECTION CHECKLIST

Inspection Sheet	Drawing Dimension	Tolerance	Actual Dimension	Accept	Reject	Method of Inspection	Comments
A	0.063 x 45°	+0.030/-0.010	.07 x 45°	/		Vern	FK-04
B	0.200	+/-0.030	.200	/		"	"
C	0.25 x 45°	+/-0.030	.25 x 45°	/		"	"
D	R0.250	+/-0.030	.250	/		R-a.	
E	0.250	+/-0.010	.246	/		Vern	FK-04
F	0.625	+/-0.030	.618	/		"	"
G	0.375	+0.030/-0.010	.385	/		"	"
H	0.950	+/-0.030	.955	/		"	"
I	19.000	+/-0.030	19.000	/		Tape	FK-05
J	Ø0.260	+0.005/-0.000	.260	/		Vern	FK-04
K	Ø0.93	+/-0.030	.927	/		"	"
L	0.30	+0.030/-0.000	.315	/		"	"
M	23.750	+/-0.030	23.750	/		Tape	FK-05
N	2.000	+/-0.030	2.008	/		Vern	FK-04
O	0.38	+/-0.030	.376	/		"	"
P							
Q							
R							
S							
T							
U							
V							


Measured by: DAS 44 9-89	Audited by: DAS 08 9-89	Preliminary Approval:
Date: 17-01-09	Date: 17-01-10	Date:

Rev	Date	Change	Revised by	Approved
A	04.01.09	New Issue P/O D206-559-015	KJ/RF	
B	12.07.31	Dwg Rev updated	KJ	
C	12.10.26	Dwg Rev updated	KJ	
D	13.07.18	Dimension 7.375 removed	KJ	
E	15.02.09	Dimensions revised	KJ	

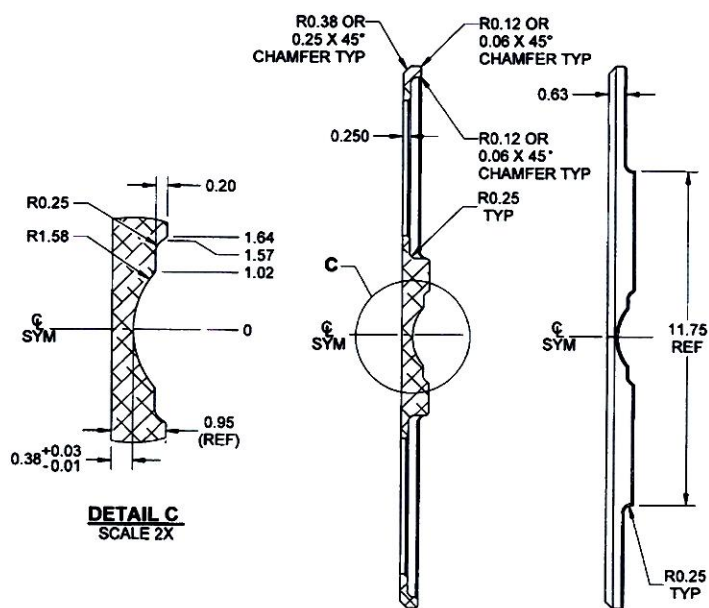

SECTION B-B

DETAIL C
SCALE 2X

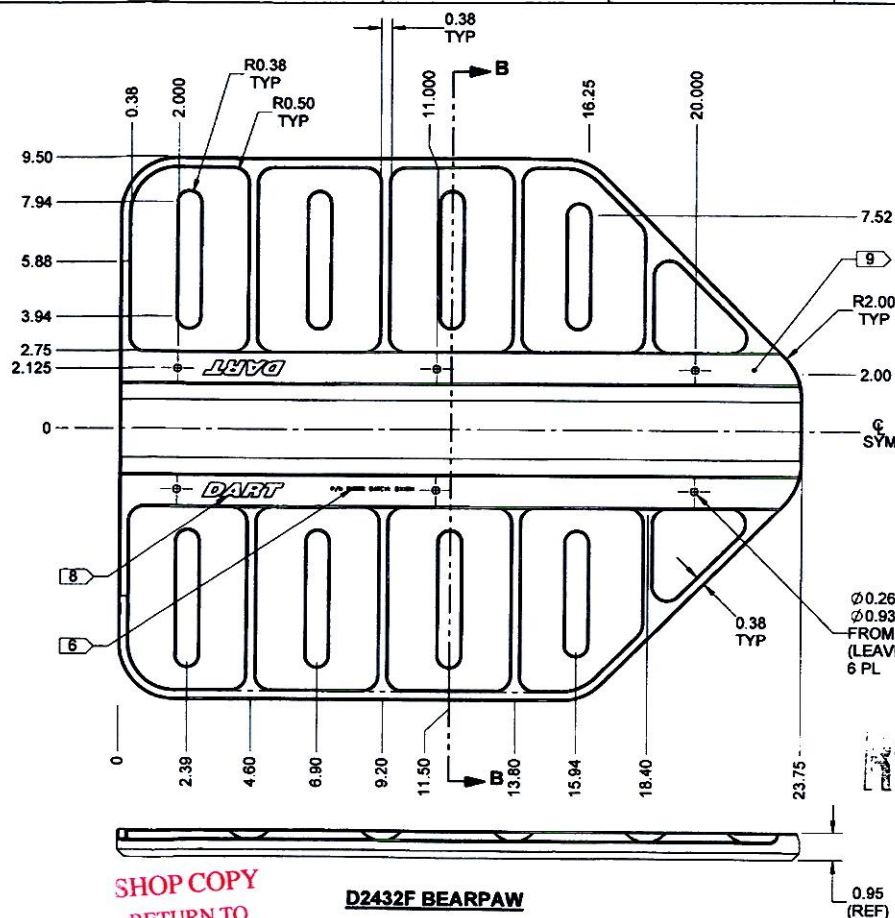

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 154784 MLJ
10-12-21

D2432F BEARPAW

NOTES:

- 1) MATERIAL: UHMW BLACK TIVAR 1000 VIRGIN MATERIAL, 1.000 THICK MACHINED TO 0.950 (REF DART SPEC. MUHMVB10)
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: ENGRAVE PART NUMBER "D2432" AND BATCH NUMBER "BXXXXX" IN ACCORDANCE WITH QSI 044 METHOD 6.3
- 7) WEIGHT: 5.87 lbs
- 8) ENGRAVE DART LOGO TO MAX DEPTH OF 0.012
- 9) APPLY 0.06 x 45° CHAMFER TO ALL EDGES ON SIDE SHOWN UNLESS OTHERWISE INDICATED
- 10) PROFILE PER DRAWING FILE "D2434F-REVH.STP"

DESIGN	LE	DART AEROSPACE LTD	
DRAWN	AP	HAWKESBURY, ONTARIO, CANADA	
CHECKED	ALS	DRAWING NO.	REV. H
MFG. APPR.	21	D2432	SHEET 2 OF 3
APPROVED	140	TITLE	SCALE
DE APPR.	140	BEARPAW	NTS
DATE	12.09.24	COPYRIGHT © 1996 BY DART AEROSPACE LTD	
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.			
